

# Hamlet of Beaver Mines

Potable Water Distribution and  
Wastewater Collection Project  
Schedule Update



# General Construction Schedule

- BYZ Enterprises commenced water and wastewater installations in the fall of 2021.
- Construction resumed in May 2022 and will continue until December 16.
- BYZ will shut down for the winter season and return in the spring to complete remaining portions of the work.
- BYZ will be responsible for ensuring all unpaved roads are maintained throughout the winter and provide appropriate interim drainage measures where required.



System  
Layouts

**MPE**  
Engineering Ltd.
























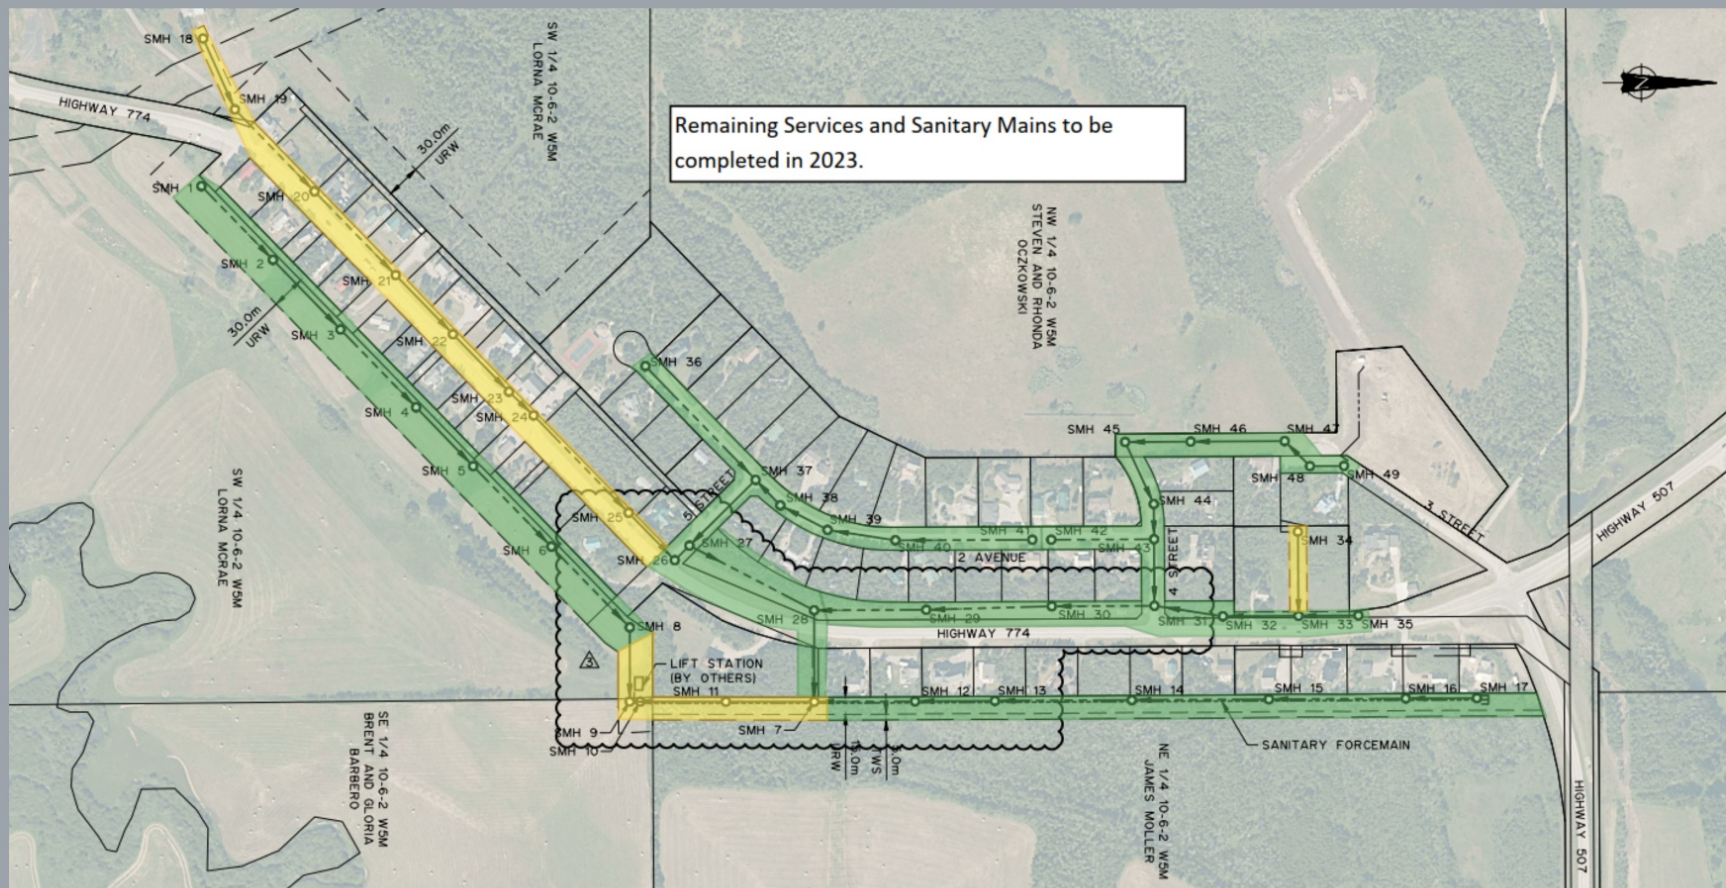







# Additional Comments

- All work required by BYZ to complete the Water Distribution and Wastewater Collection Project is anticipated to be completed in 2023 prior to the system being available for water and sewer service connections.
- With completion of the water system by BYZ in 2022, hydrants will be operational. The Pincher Creek Emergency Services team will be completing hydrant testing and updating the Fire Underwriters Survey for the Hamlet.
- The Beaver Mines Lift Station and Forcemain is anticipated to be complete by May 31, 2022.
- The building envelope of the Lift Station is currently being finished and electrical/mechanical/process work will be completed throughout winter.
